DRAFT FOR DISCUSSION PURPOSES 1/12/02

ID	Task Name	Duration	Start	Finish	Predecessors
1	**Short Term Study: EHC**	**221 days**	**Thu 11/1/01**	**Fri 9/30/02**	
2	Investigator Brochure	15 days	Thu 11/1/01	Wed 11/21/01	
3	Study Objectives	5 days	Thu 11/1/01	Wed 11/7/01	
4	Draft protocol / Summary Plan	10 days	Thu 11/8/01	Wed 11/21/01	3
5	Site Selection	15 days	Thu 11/22/01	Wed 12/12/01	4
6	1st Project Agreement with CRO	15 days	Thu 12/13/01	Wed 1/2/02	5,4
7	Protocol Development	30 days	Thu 11/22/01	Wed 1/2/02	2
8	Final Protocol, Informed Consent	0 days	Wed 1/2/02	Wed 1/2/02	2,7
9	IRB Review	20 days	Thu 1/3/02	Wed 1/30/02	6,2
10	Bioanalytical Methods Setup	80 days	Thu 11/22/01	Wed 3/13/02	4
11	IRB Approval	0 days	Wed 1/30/02	Wed 1/30/02	9
12	2nd Project Agreement	10 days	Thu 1/31/02	Wed 2/13/02	11
13	Recruitment and Screening	20 days	Thu 2/14/02	Wed 3/13/02	6,12
14	Test Materials Available	0 days	Thu 3/14/02	Thu 3/14/02	
15	**Clinical Performance**	**11 days**	**Thu 3/14/02**	**Sun 3/24/02**	**14,13,11**
16	Subject Check In	1 day	Thu 3/14/02	Thu 3/14/02	
17	Subject Randomization	0 day	Sun 3/17/02	Sun 3/17/02	
18	Study Conduct	8 days	Mon 3/18/02	Sun 3/24/02	
19	Subject Release	0 day	Sun 3/24/02	Sun 3/24/02	Release on Monday
20	**Lab Analysis**	**40 days**	**Mon 3/25/02**	**Fri 5/17/02**	**10,15**
21	Analysis of Biomarkers	0 wks	Mon 3/25/02	Fri 5/3/02	
22	Data Listings to PM	1 wk	Mon 5/6/02	Fri 5/10/02	21
23	Biomarker Tables to PM	1 wk	Mon 5/13/02	Fri 5/17/02	22
24	**Data Management**	**65 days**	**Mon 3/25/02**	**Fri 6/21/02**	**15,20SS**
25	Data Entry	4 wks	Mon 3/25/02	Fri 4/19/02	
26	Edit Chks, Db Clean-Up	4 wks	Mon 4/22/02	Fri 5/17/02	25
27	Internal Data Listing Review	1 wk	Mon 5/20/02	Fri 5/24/02	26
28	DB Lock	0 days	Fri 5/24/02	Fri 5/24/02	27
29	Data Listings for PM Review	2 wks	Mon 5/27/02	Fri 6/7/02	28
30	Safety Table for PM Review	2 wks	Mon 6/10/02	Fri 6/21/02	29
31	Draft Report	6 wks	Mon 6/24/02	Fri 8/2/02	24
32	Results Available	0 days	Fri 8/2/02	Fri 8/2/02	31
33	Final Report	20 days	Mon 8/5/02	Fri 8/30/02	32
34	Final Results	0 days	Fri 8/30/02	Fri 8/30/02	33

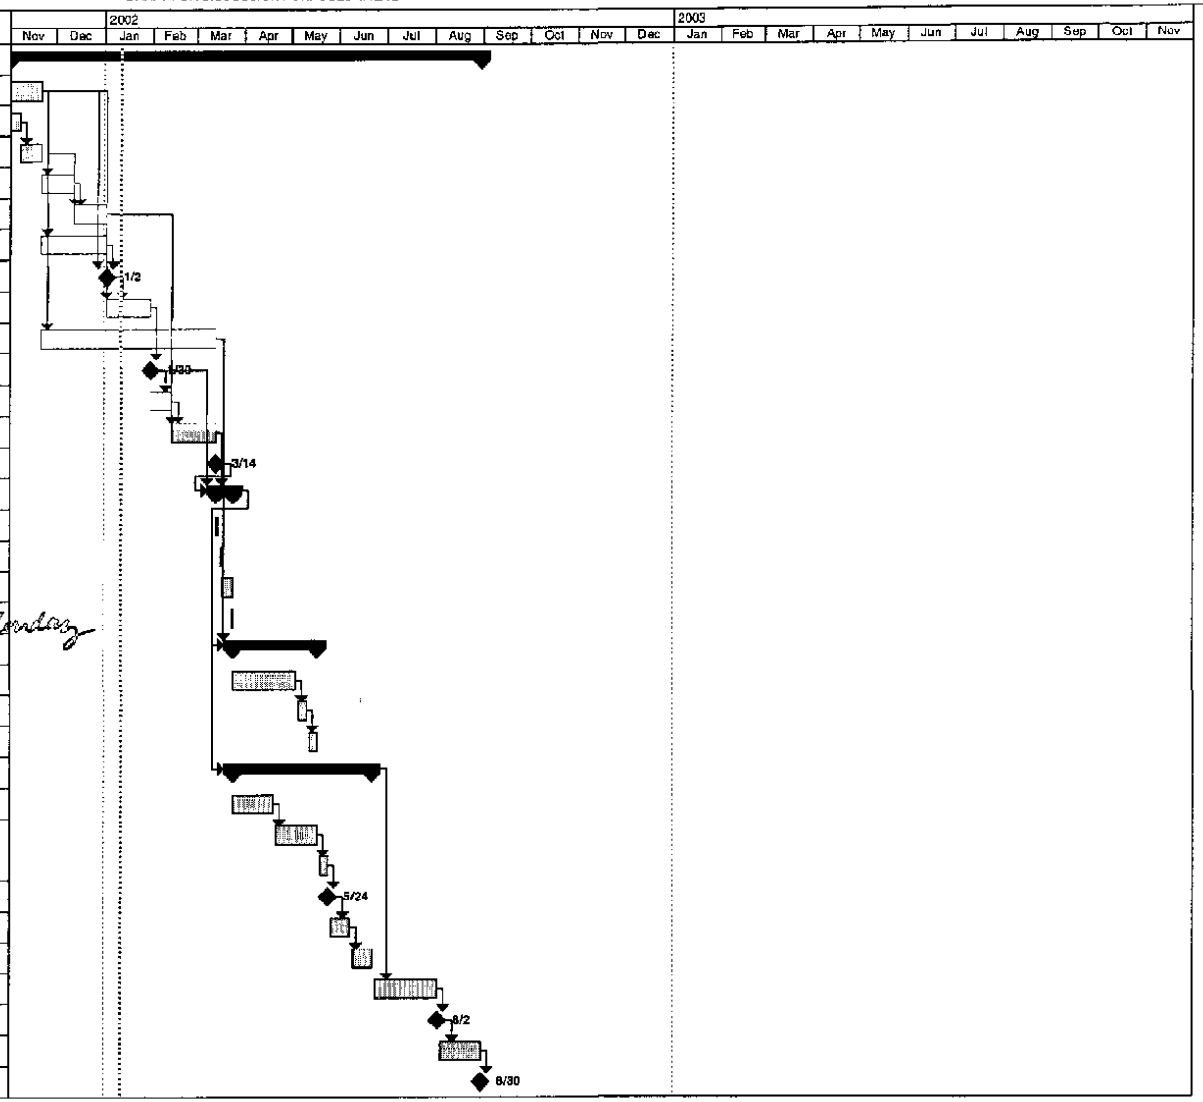

& Amadist

Project: Short Term2
Date: Fri 1/11/02

Task | Split | Progress | Milestone | Summary | Rolled Up Task | Rolled Up Split | Rolled Up Milestone | Rolled Up Progress | External Tasks | Project Summary

PM30067462

Source: https://www.industrydocuments.ucsf.edu/docs/mnmx0001
